


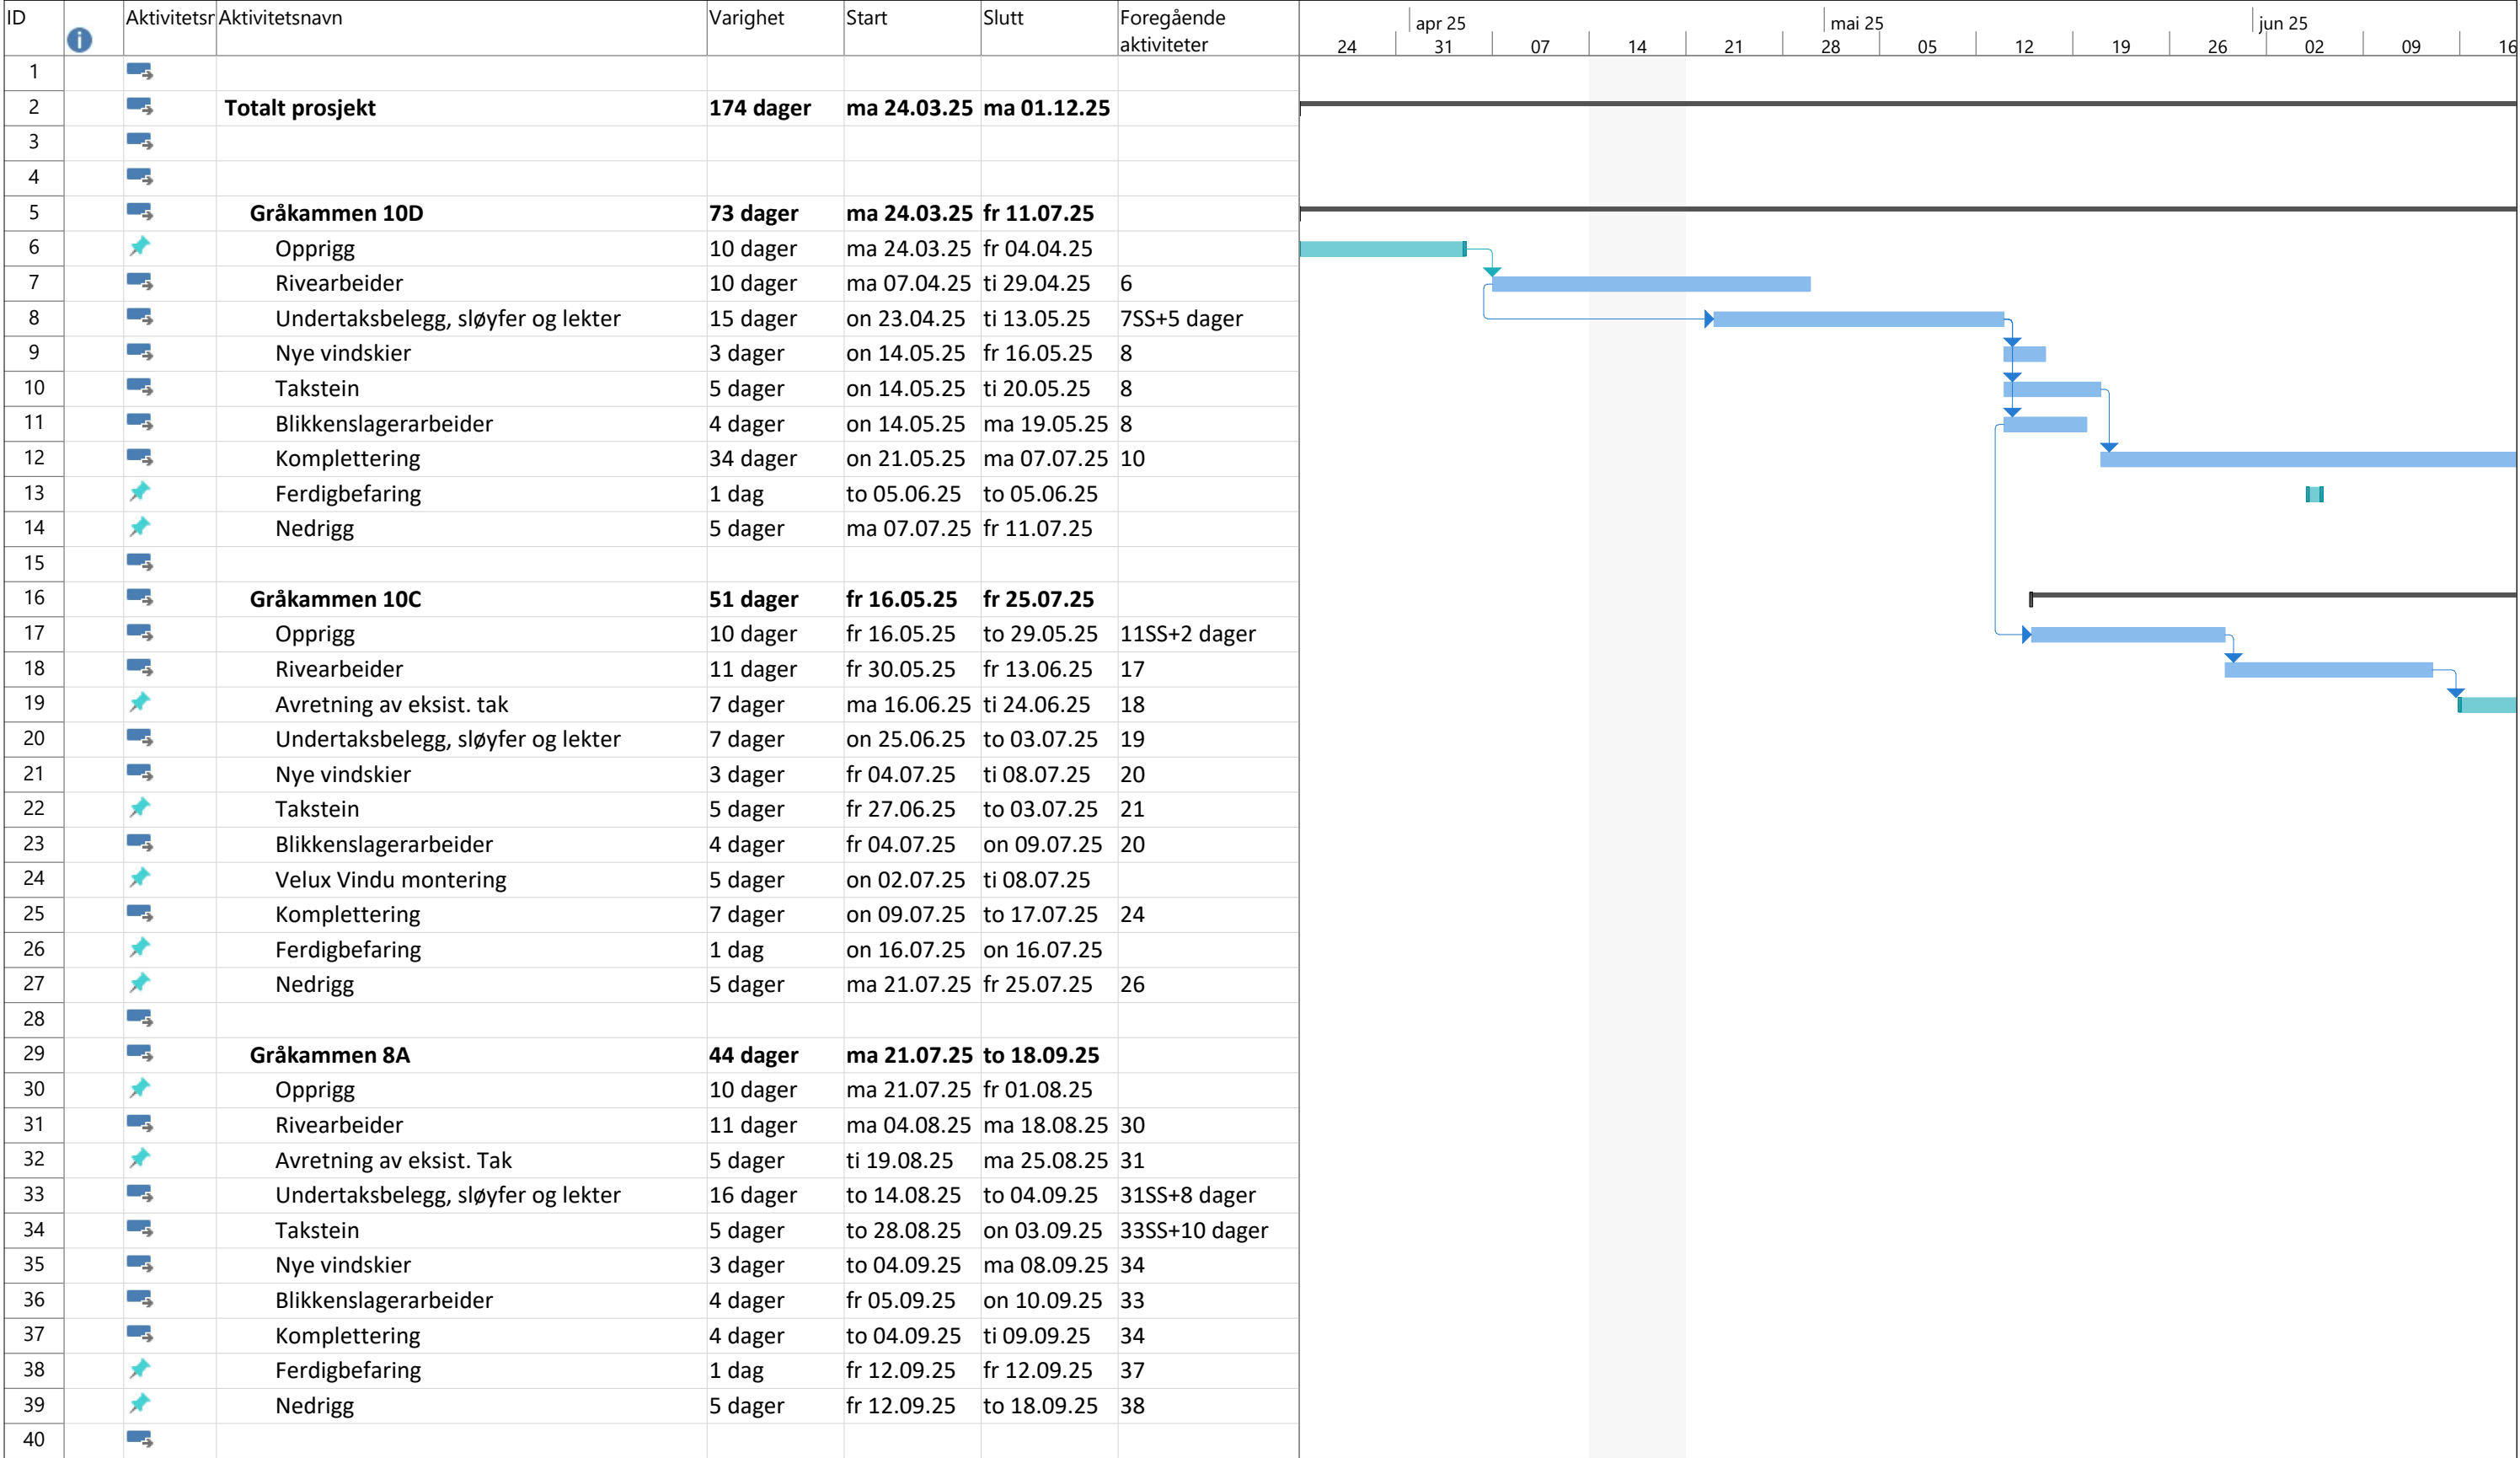

Prosjekt: Fremdriftsplan - Gråka
Dato: on 25.06.25

Aktivitet		Inaktiv aktivitet		Manuell sammendragfremheving		Ekstern milepæl	
Deling		Inaktiv milepæl		Manuelt sammendrag		Tidsfrist	
Milepæl		Inaktivt sammendrag		Bare start		Fremdrift	
Sammendrag		Manuell aktivitet		Bare slutt		Manuell fremdrift	
Prosjektsammendrag		Bare varighet		Eksterne aktiviteter			

ID		Aktivitetsr	Aktivitetsnavn	Varighet	Start	Slutt	Foregående aktiviteter	24	apr 25 31	07	14	21	mai 25 28	05	12	19	26	jun 25 02	09	16
41			Gråkammen 8B	43 dager	fr 08.08.25	ti 07.10.25														
42			Opprigg	10 dager	fr 08.08.25	to 21.08.25														
43			Rivearbeider	11 dager	fr 22.08.25	fr 05.09.25	42													
44			Avretting av Eksist. Tak	5 dager	ma 08.09.25	fr 12.09.25	43													
45			Undertaksbelegg, sløyfer og lekter	16 dager	on 03.09.25	on 24.09.25	43SS+8 dager													
46			Takstein	5 dager	on 17.09.25	ti 23.09.25	45SS+10 dager													
47			Nye vindskier	3 dager	on 24.09.25	fr 26.09.25	46													
48			Blikkenslagerarbeider	4 dager	to 25.09.25	ti 30.09.25	45													
49			Komplettering	4 dager	on 24.09.25	ma 29.09.25	46													
50			Ferdigbefaring	1 dag	ti 30.09.25	ti 30.09.25	49													
51			Nedrigg	5 dager	on 01.10.25	ti 07.10.25	50													
52																				
53			Gråkammen 10E	42 dager	to 18.09.25	fr 14.11.25														
54			Opprigg	10 dager	to 18.09.25	on 01.10.25														
55			Rivearbeider	11 dager	on 01.10.25	on 15.10.25	50													
56			Avretting av Eksist Tak	5 dager	to 16.10.25	on 22.10.25	55													
57			Undertaksbelegg, sløyfer og lekter	16 dager	ma 13.10.25	ma 03.11.25	55SS+8 dager													
58			Takstein	5 dager	ma 27.10.25	fr 31.10.25	57SS+10 dager													
59			Nye vindskier	3 dager	ma 03.11.25	on 05.11.25	58													
60			Blikkenslagerarbeider	4 dager	ti 04.11.25	fr 07.11.25	57													
61			Komplettering	4 dager	ma 03.11.25	to 06.11.25	58													
62			Ferdigbefaring	1 dag	fr 07.11.25	fr 07.11.25	61													
63			Nedrigg	5 dager	ma 10.11.25	fr 14.11.25	62													
64																				
65			Gråkammen 10F	43 dager	to 02.10.25	ma 01.12.25														
66			Opprigg	10 dager	to 02.10.25	on 15.10.25	54													
67			Rivearbeider	11 dager	to 16.10.25	to 30.10.25	66													
68			Avretning av eksist tak	5 dager	fr 31.10.25	to 06.11.25	67													
69			Undertaksbelegg, sløyfer og lekter	16 dager	ti 28.10.25	ti 18.11.25	67SS+8 dager													
70			Takstein	5 dager	ti 11.11.25	ma 17.11.25	69SS+10 dager													
71			Nye vindskier	3 dager	fr 31.10.25	ti 04.11.25	67													
72			Blikkenslagerarbeider	4 dager	on 19.11.25	ma 24.11.25	69													
73			Komplettering	4 dager	ti 18.11.25	fr 21.11.25	70													
74			Ferdigbefaring	1 dag	ma 24.11.25	ma 24.11.25	73													
75			Nedrigg	5 dager	ti 25.11.25	ma 01.12.25	74													

Prosjekt: Fremdriftsplan - Gråka

Dato: on 25.06.25

Aktivitet

Deling

Milepæl

Sammendrag

Prosjektsammendrag

Inaktiv aktivitet

Inaktiv milepæl

Inaktivt sammendrag

Manuell aktivitet

Bare varighet

Manuell sammendragsfremheving

Manuelt sammendrag

Bare start

Bare slutt

Eksterne aktiviteter

Ekstern milepæl

Tidsfrist

Fremdrift

Manuell fremdrift

Side 2



Prosjekt: Fremdriftsplan - Gråka
Dato: on 25.06.25

Aktivitet		Inaktiv aktivitet		Manuell sammendragsfremheving		Ekstern milepæl	
Deling		Inaktiv milepæl		Manuelt sammendrag		Tidsfrist	
Milepæl		Inaktivt sammendrag		Bare start		Fremdrift	
Sammendrag		Manuell aktivitet		Bare slutt		Manuell fremdrift	
Prosjektsammendrag		Bare varighet		Eksterne aktiviteter			

